

Project Planning Phase

Project Planning Template (Product Backlog, Sprint Planning, Stories, Story points)

Date	01 September 2026
Team ID	Individual Project
Project Name	Software Installation Request Automation in ServiceNow
Maximum Marks	5 Marks

Product Backlog, Sprint Schedule, and Estimation (4 Marks)

Use the below template to create product backlog and sprint schedule.

Sprint	Functional Requirement (Epic)	User Story Number	User Story / Task	Story Points	Priority	Team Members
Sprint-1	Service Catalog Setup	USN-1	As an individual project owner, I can create an Update Set to capture the project configuration changes.	2	High	Individual
Sprint-1		USN-2	As an employee, I can submit a standardized Software Installation Request catalog item.	3	High	Individual
Sprint-1		USN-3	As a requester, I can enter Software Name, Version Required, License Justification, and Urgency.	5	High	Individual
Sprint-1		USN-4	As a requester, I can test the catalog item and verify that the submitted request is created correctly.	2	High	Individual
Sprint-1	Request Tracking	USN-5	As an administrator, I can verify the request and requested-item records for the submitted catalog request.	3	Medium	Individual
Sprint-1		USN-6	As an administrator, I can configure basic requester notifications for the request lifecycle.	5	Medium	Individual
Sprint-2	Workflow & Fulfillment	USN-7	As an administrator, I can create an automation flow/workflow for the software installation request.	5	High	Individual
Sprint-2		USN-8	As an approver, I can receive and process the approval for a software installation request.	3	High	Individual
Sprint-2		USN-9	As an IT support member, I can receive an automatically created fulfillment task.	5	High	Individual
Sprint-2		USN-10	As an administrator, I can attach the workflow/flow to the Software Installation Request catalog item.	2	High	Individual
Sprint-2		USN-11	As an IT support member, I can update the task state from Open to Work in Progress to Completed.	3	Medium	Individual
Sprint-2		USN-12	As a requester, I can receive progress notifications during approval and fulfillment.	2	Medium	Individual
Sprint-3	Exception Handling & Business Rules	USN-13	As an administrator, I can validate sc_request and sc_req_item records after request submission.	3	High	Individual

Sprint-3		USN-14	As an administrator, I can create a Business Rule that detects a software request placed On Hold.	5	High	Individual
Sprint-3		USN-15	As an administrator, I can create an incident automatically when a license shortage prevents fulfillment.	5	High	Individual
Sprint-3		USN-16	As an administrator, I can configure SLA tracking for timely software request fulfillment.	3	Medium	Individual
Sprint-3		USN-17	As an administrator, I can test the license shortage and incident-creation scenario.	2	Medium	Individual
Sprint-3		USN-18	As an administrator, I can review request and fulfillment records for reporting purposes.	2	Low	Individual
Sprint-4	Testing & Deployment	USN-19	As an administrator, I can execute end-to-end testing of catalog, approval, task, notification, and exception handling.	5	High	Individual
Sprint-4		USN-20	As an administrator, I can complete the project Update Set after configuration is finalized.	2	High	Individual
Sprint-4		USN-21	As an administrator, I can export the completed Update Set as XML.	2	High	Individual
Sprint-4		USN-22	As an administrator, I can retrieve the Update Set in another instance for deployment testing.	3	High	Individual
Sprint-4		USN-23	As an administrator, I can preview and commit the Update Set without missing configuration elements.	3	High	Individual
Sprint-4		USN-24	As an administrator, I can validate that all transferred configurations work correctly after deployment.	5	High	Individual

Project Tracker, Velocity & Burndown Chart: (4 Marks)

Sprint	Total Story Points	Duration	Sprint Start Date	Sprint End Date (Planned)	Story Points Completed (as on Planned End Date)	Sprint Release Date (Actual)
Sprint-1	20	6 Days	09 Aug2026	14 Aug2026	20	14 Aug 2026
Sprint-2	20	6 Days	15 Aug2026	20 Aug2026	20	20 Aug 2026
Sprint-3	20	6 Days	21 Aug2026	26 Aug2026	20	26 Aug 2026
Sprint-4	20	6 Days	27 Aug2026	01 Sep2026	20	01 Sep 2026

Velocity:

Imagine we have a 6-day sprint duration, and the velocity of the individual project is 20 story points per sprint. Let's calculate the average velocity (AV) per iteration unit (story points per day).

Total Story Points = 20 + 20 + 20 + 20 = 80


Number of Sprints = 4

Velocity = 80 / 4 = 20 Story Points per Sprint

Average Velocity per Day = 20 / 6 = 3.33 Story Points per Day

Burndown Chart:

A burn down chart is a graphical representation of work left to do versus time. It is often used in agile software development methodologies such as Scrum. However, burn down charts can be applied to any project containing measurable progress over time.

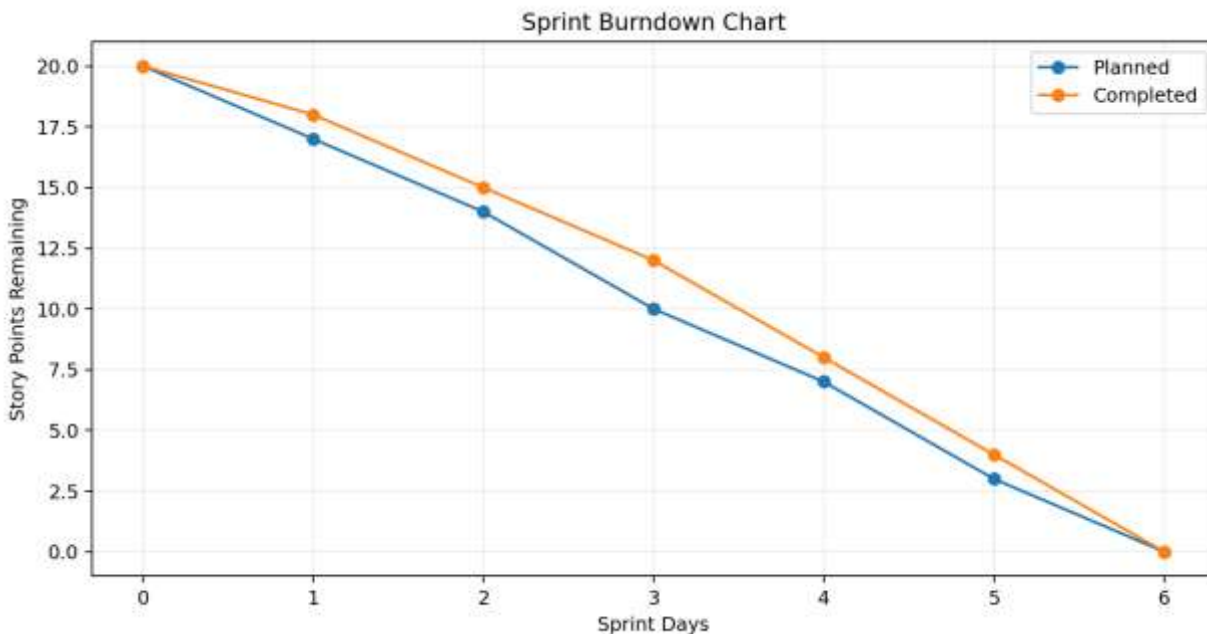

Planning Summary: The backlog is divided into four planned Sprints. Sprint 1 focuses on Service Catalog setup and request tracking; Sprint 2 focuses on workflow and fulfillment; Sprint 3 covers Business Rules, SLA and exception handling; Sprint 4 covers end-to-end testing and Update Set deployment.

Reference: <https://www.atlassian.com/agile/project-management>
